

Impact sheets for selected major Temporary Capacity Restrictions (TCR)

Foreword

On RFC Rhine Alpine we introduce the **TCR Impact sheets** to present in one glance general and important information about upcoming TCRs. These impact sheets highlight **some infrastructure works which have a big impact** on international rail freight traffic along RFC Rhine-Alpine in 2020.

Disclaimer:

The content of this document has been compiled with meticulous care based on information available at the publication date. However we cannot assume any liability for accuracy and accept no liability for damages suffered as a result of defects of this document.

For detailed and complete customer information we kindly refer to the information which is available via the involved national Infrastructure Managers.

Further information (e.g. in form of an excel list on all planned TCR) is available on the website of RFC RALP under link: <https://www.corridor-rhine-alpine.eu/downloads.html>

Version 2.0

Publication Date 24.12.2019

PARTNER



Co-financed by the European Union
Connecting Europe Facility


Impact of TCR 2020 at ProRail

Section Amsterdam - Meteren



State of play : 23.12.2019

Disclaimer see front page

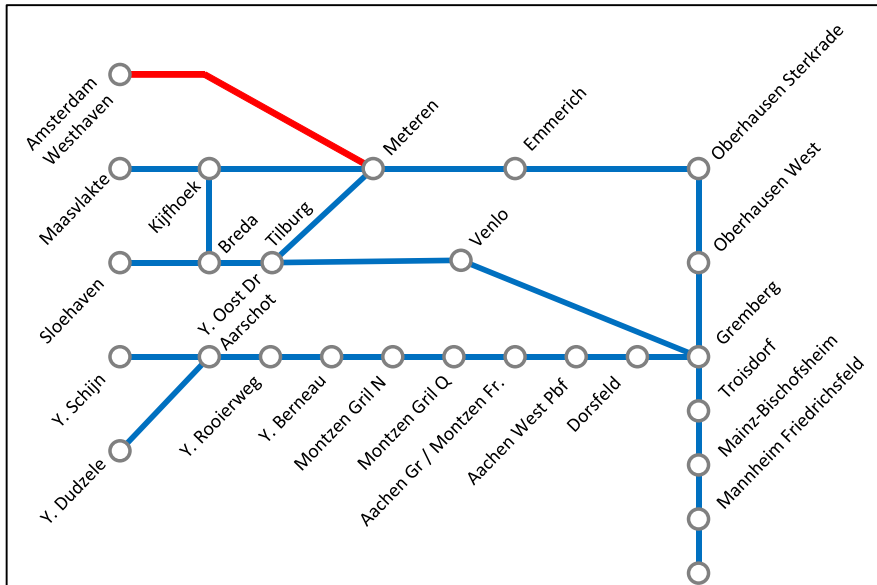

Major Capacity Restriction

- Section: Amsterdam Westhaven – Duivendrecht
- Typ: Total Closure
- Period: 06-06-2020 / 07-06-2020
- Type of works: track renewal

Location: Amsterdam Westhaven - Duivendrecht

Works: track renewal

Single track operation Total closure

January							February							March							April							
KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	
1	1	2	3	4	5		5					1	2	9						1	14			1	2	3	4	5
2	6	7	8	9	10	11	6	3	4	5	6	7	8	9	2	3	4	5	6	7	8	13	14	15	16	17	18	19
3	13	14	15	16	17	18	7	10	11	12	13	14	15	16	10	9	10	11	12	13	14	16	17	18	19	20	21	22
4	20	21	22	23	24	25	8	17	18	19	20	21	22	23	11	16	17	18	19	20	21	22	23	24	25	26	27	28
5	27	28	29	30	31		9	24	25	26	27	28	29		12	23	24	25	26	27	28	29						

May							June							July							August								
KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa		
18					1	2	23	1	2	3	4	5	6	27		1	2	3	4	5	31					1	2		
19	4	5	6	7	8	9	24	8	9	10	11	12	13	14	28	6	7	8	9	10	11	32	3	4	5	6	7	8	9
20	11	12	13	14	15	16	25	15	16	17	18	19	20	21	29	13	14	15	16	17	18	33	10	11	12	13	14	15	16
21	18	19	20	21	22	23	26	22	23	24	25	26	27	28	30	20	21	22	23	24	25	34	17	18	19	20	21	22	23
22	25	26	27	28	29	30	31	27	29	30					31	27	28	29	30	31		35	24	25	26	27	28	29	30
																						36	31						

September							October							November							December							
KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	
36		1	2	3	4	5	40					1	2	3	44						48	1	2	3	4	5	6	
37	7	8	9	10	11	12	41	5	6	7	8	9	10	11	45	2	3	4	5	6	7	8	9	10	11	12	13	14
38	14	15	16	17	18	19	42	12	13	14	15	16	17	18	46	9	10	11	12	13	14	15	16	17	18	19	20	21
39	21	22	23	24	25	26	43	19	20	21	22	23	24	25	47	16	17	18	19	20	21	22	23	24	25	26	27	28
40	28	29	30				44	26	27	28	29	30	31		48	23	24	25	26	27	28	29						
															49	30						50						

Impact on International Rail Freight

- Deviations: Yes, Amsterdam-Hilversum-Utrecht
- Estimated extra running time: 30 minutes
- Restrictions for ad-hoc requests: limited capacity
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted 4 weeks before operation


Impact of TCR 2020 at ProRail

Section Tilburg – Meteren – Amsterdam



State of play : 23.12.2019

Disclaimer see front page

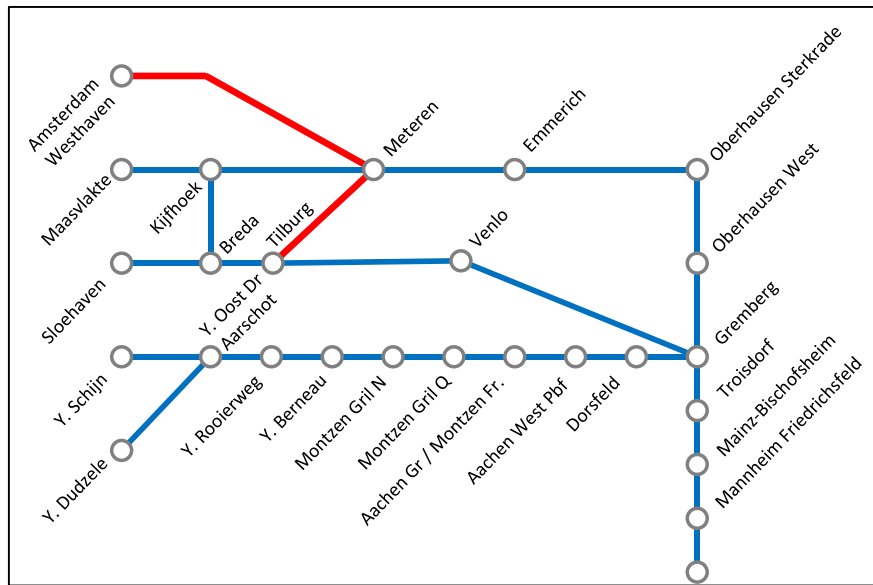

Major Capacity Restriction

- Utrecht – Geldermalsen – 's-Hertogenbosch
- Typ: Total Closure and single track Geldermalsen area
- Period: 03-07-2020 / 08-08-2020
- Type of works: track renewal

Location: Geldermalsen - 's-Hertogenbosch

Works: track renewal

Single track operation Total closure

January							February							March							April						
KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa
1			1	2	3	4	5	6					1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
2	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
3	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31								
4	20	21	22	23	24	25	26	27	28	29	30	31															
5	27	28	29	30	31																						
May							June							July							August						
KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa
18						1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22
19	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
20	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31						
21	18	19	20	21	22	23	24	25	26	27	28	29	30	31													
22	25	26	27	28	29	30	31																				
September							Oktober							November							December						
KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa
36	1	2	3	4	5	6	40	1	2	3	4	5	6	44	1	2	3	4	5	6	48	1	2	3	4	5	6
37	7	8	9	10	11	12	41	5	6	7	8	9	10	45	2	3	4	5	6	7	49	7	8	9	10	11	
38	14	15	16	17	18	19	42	12	13	14	15	16	17	46	9	10	11	12	13	14	50	14	15	16	17	18	
39	21	22	23	24	25	26	43	19	20	21	22	23	24	47	16	17	18	19	20	21	51	21	22	23	24	25	
40	28	29	30				44	26	27	28	29	30	31	48	23	24	25	26	27	28	52	28	29	30	31		
														49	30												

Impact on International Rail Freight

- Deviations: Yes, via Utrecht - Arnhem
- Estimated extra running time: no extra running time
- Restrictions for ad-hoc requests: limited capacity
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted 4 weeks before operation


Impact of TCR 2020 at Infrabel

Section Zeebrugge - Gent



State of play : 20.12.2019

Disclaimer see front page

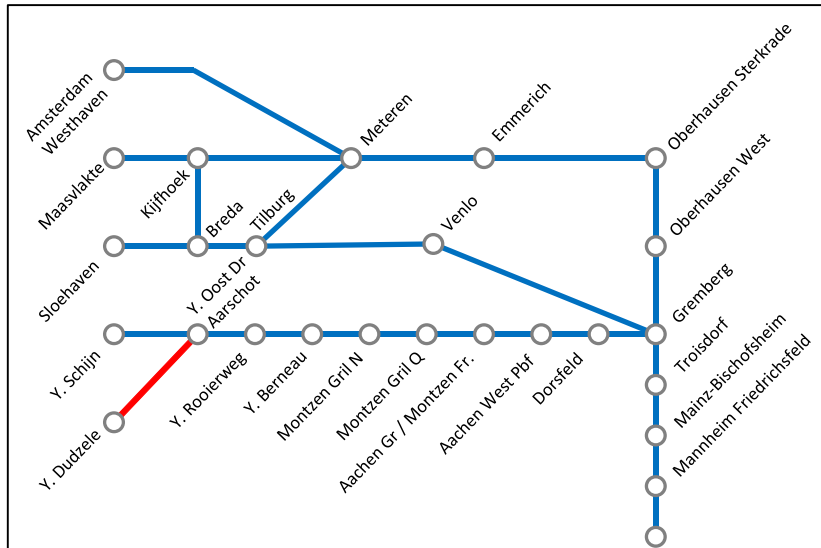

Location Gent Sint-Pieters - Brugge

Works: Tracks

Single track operation Total closure

January

KW	Mo	Ti	Mi	Do	Fr	Sa	So
1						1	2
2	3	4	5	6	7	8	9
3	10	11	12	13	14	15	16
4	17	18	19	20	21	22	23
5	24	25	26	27	28	29	30
6	31						

February

KW	Mo	Ti	Mi	Do	Fr	Sa	So
5							1
6	3	4	5	6	7	8	9
7	10	11	12	13	14	15	16
8	17	18	19	20	21	22	23
9	24	25	26	27	28	29	
10							

March

KW	Mo	Ti	Mi	Do	Fr	Sa	So
9							1
10	2	3	4	5	6	7	8
11	9	10	11	12	13	14	15
12	16	17	18	19	20	21	22
13	23	24	25	26	27	28	29
14	30	31					

April

KW	Mo	Ti	Mi	Do	Fr	Sa	So
14			1	2	3	4	5
15	6	7	8	9	10	11	12
16	13	14	15	16	17	18	19
17	20	21	22	23	24	25	26
18	27	28	29	30			

May

KW	Mo	Ti	Mi	Do	Fr	Sa	So
18					1	2	3
19	4	5	6	7	8	9	10
20	11	12	13	14	15	16	17
21	18	19	20	21	22	23	24
22	25	26	27	28	29	30	31

June

KW	Mo	Ti	Mi	Do	Fr	Sa	So
23	1	2	3	4	5	6	7
24	8	9	10	11	12	13	14
25	15	16	17	18	19	20	21
26	22	23	24	25	26	27	28
27	29	30					

July

KW	Mo	Ti	Mi	Do	Fr	Sa	So
27			1	2	3	4	5
28	6	7	8	9	10	11	12
29	13	14	15	16	17	18	19
30	20	21	22	23	24	25	26
31	27	28	29	30	31		

August

KW	Mo	Ti	Mi	Do	Fr	Sa	So
31							1
32	3	4	5	6	7	8	9
33	10	11	12	13	14	15	16
34	17	18	19	20	21	22	23
35	24	25	26	27	28	29	30
36	31						

September

KW	Mo	Ti	Mi	Do	Fr	Sa	So
36						1	2
37	3	4	5	6	7	8	9
38	10	11	12	13	14	15	16
39	17	18	19	20	21	22	23
40	24	25	26	27	28	29	30

Oktober

KW	Mo	Ti	Mi	Do	Fr	Sa	So
40					1	2	3
41	4	5	6	7	8	9	10
42	11	12	13	14	15	16	17
43	18	19	20	21	22	23	24
44	25	26	27	28	29	30	31

November

KW	Mo	Ti	Mi	Do	Fr	Sa	So
44							1
45	2	3	4	5	6	7	8
46	9	10	11	12	13	14	15
47	16	17	18	19	20	21	22
48	23	24	25	26	27	28	29
49	30						

December

KW	Mo	Ti	Mi	Do	Fr	Sa	So
49			1	2	3	4	5
50	6	7	8	9	10	11	12
51	13	14	15	16	17	18	19
52	20	21	22	23	24	25	26
53	27	28	29	30	31		

Major Capacity Restriction

- Section: Zeebrugge - Gent
- Type: Total Closure Operation
- Period:

weekends 2,4,5,6,8,12,17,20,43,48

nights from 00.00 to 4:00 ⇒ 06/01 to 09/01

14/01 tot 17/01 – 20/01 to 24/1 - 27/01 to 31/1

3/02 to 8/02 - 7/2 to 21/2 – 24/2 to 29/2

16/03- 20/3 – 23/03 to 28/3 - 13/4 tot 17/4

20/4 to 25/4 – 27/4 to 1/05 – 11/5 to 15/05

18/05 to 23/5 - 21/8 to 28/8 - 5/10 to 10/10

12/10 to 17/10 - 19/10 to 23/10 – 26/10 to 31/10

16/11 to 21 /11 – 23/11 to 27/11 - 7/12 tot 12/12

14/12 to 19/12

nights from 00:00 to 06:00 ⇒ 15/06 to 20/066

7/09 to 12/09 - 21/09 to 26/09 – 28/09 tot 3/10

- Type of works: Tracks

Impact on International Rail Freight

- Deviations: Yes
- Estimated extra running time: Tbd
- Restrictions for ad-hoc requests might occur
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: No


Impact of TCR 2020 at Infrabel

Section Antwerpen - Montzen



State of play : 20.12.2019

Disclaimer see front page

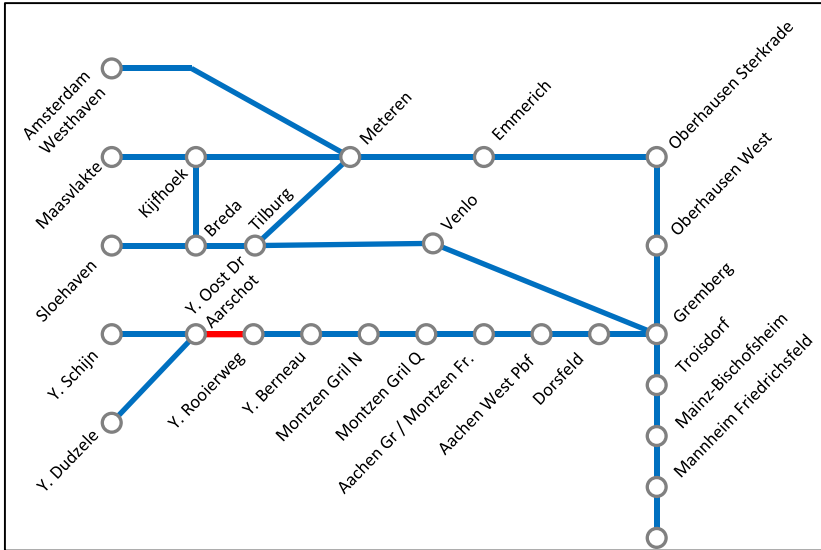

Major Capacity Restriction

- Section: Antwerpen -Montzen
- Type: Total Closure operation
- Period: From Friday 23:15 to Monday 04:30 continuous (see calendar)
- Type of works: ETCS L2
Removal railway crossings

Location Hasselt - Y. Rooierweg

Works : ETCS L2 / Removal level crossings between Hasselt and Bilzen

Single track operation Total closure

January

KW	Mo	Di	Mi	Do	Fr	Sa	So
1			1	2	3	4	5
2	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26
5	27	28	29	30	31		

February

KW	Mo	Di	Mi	Do	Fr	Sa	So
5					1	2	
6	3	4	5	6	7	8	9
7	10	11	12	13	14	15	16
8	17	18	19	20	21	22	23
9	24	25	26	27	28	29	

March

KW	Mo	Di	Mi	Do	Fr	Sa	So
9							1
10	2	3	4	5	6	7	8
11	9	10	11	12	13	14	15
12	16	17	18	19	20	21	22
13	23	24	25	26	27	28	29
14	30	31					

April

KW	Mo	Di	Mi	Do	Fr	Sa	So
14			1	2	3	4	5
15	6	7	8	9	10	11	12
16	13	14	15	16	17	18	19
17	20	21	22	23	24	25	26
18	27	28	29	30			

May

KW	Mo	Di	Mi	Do	Fr	Sa	So
18			1	2	3		
19	4	5	6	7	8	9	10
20	11	12	13	14	15	16	17
21	18	19	20	21	22	23	24
22	25	26	27	28	29	30	31

June

KW	Mo	Di	Mi	Do	Fr	Sa	So
23	1	2	3	4	5	6	7
24	8	9	10	11	12	13	14
25	15	16	17	18	19	20	21
26	22	23	24	25	26	27	28
27	29	30					

July

KW	Mo	Di	Mi	Do	Fr	Sa	So
27			1	2	3	4	5
28	6	7	8	9	10	11	12
29	13	14	15	16	17	18	19
30	20	21	22	23	24	25	26
31	27	28	29	30	31		

August

KW	Mo	Di	Mi	Do	Fr	Sa	So
31			1	2	3		
32	4	5	6	7	8	9	10
33	11	12	13	14	15	16	17
34	17	18	19	20	21	22	23
35	24	25	26	27	28	29	30
36	31						

September

KW	Mo	Di	Mi	Do	Fr	Sa	So
36		1	2	3	4	5	6
37	7	8	9	10	11	12	13
38	14	15	16	17	18	19	20
39	21	22	23	24	25	26	27
40	28	29	30				

October

KW	Mo	Di	Mi	Do	Fr	Sa	So
40			1	2	3	4	
41	5	6	7	8	9	10	11
42	12	13	14	15	16	17	18
43	19	20	21	22	23	24	25
44	26	27	28	29	30	31	

November

KW	Mo	Di	Mi	Do	Fr	Sa	So
44							1
45	2	3	4	5	6	7	8
46	9	10	11	12	13	14	15
47	16	17	18	19	20	21	22
48	23	24	25	26	27	28	29
49	30						

December

KW	Mo	Di	Mi	Do	Fr	Sa	So
49		1	2	3	4	5	6
50	7	8	9	10	11	12	13
51	14	15	16	17	18	19	20
52	21	22	23	24	25	26	27
53	28	29	30	31			

Impact on International Rail Freight

- Deviations: Yes
- Estimated extra running time: Tbd
- Restrictions for ad-hoc requests might occur
- Restrictions in train parameters: Class 66 weight limit to 1760t
- Restrictions in container profile: needs C60, C390, P60, P380
- In annual timetable: No


Impact of TCR 2020 at Infrabel

Section Antwerpen - Montzen



State of play : 20.12.2019

Disclaimer see front page

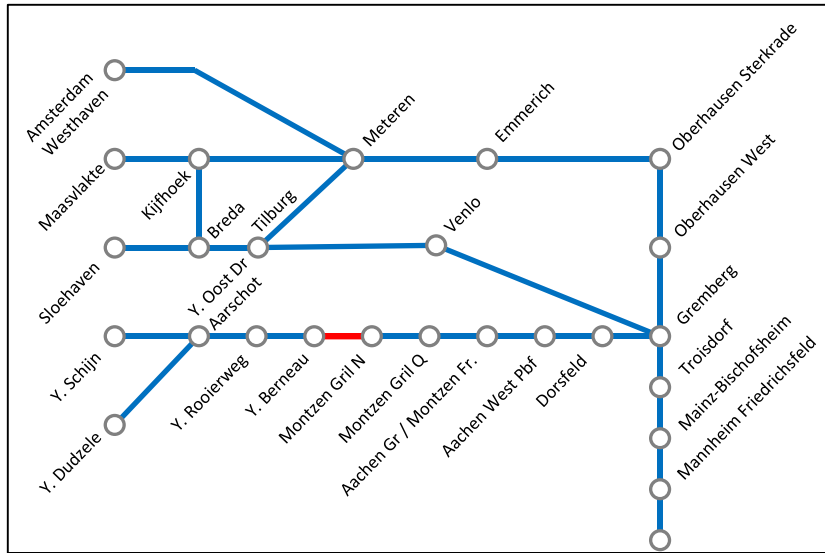

Major Capacity Restriction

- Section: Antwerpen – Montzen
- Type: Total line closure (TLC) See calendar
Single track operation (see calendar)
- Duration : Continuous See calendar)
- Type of works: signalling works

Location Visé - Montzen

Works: Signalling works

Single track operation Total closure

January

KW	Mo	Ti	Mi	Do	Fr	Sa	So
1			1	2	3	4	5
2	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26
5	27	28	29	30	31		

February

KW	Mo	Ti	Mi	Do	Fr	Sa	So
5					1	2	
6	3	4	5	6	7	8	9
7	10	11	12	13	14	15	16
8	17	18	19	20	21	22	23
9	24	25	26	27	28	29	

March

KW	Mo	Ti	Mi	Do	Fr	Sa	So
9						1	
10	2	3	4	5	6	7	8
11	9	10	11	12	13	14	15
12	16	17	18	19	20	21	22
13	23	24	25	26	27	28	29
14	30	31					

April

KW	Mo	Ti	Mi	Do	Fr	Sa	So
14		1	2	3	4	5	
15	6	7	8	9	10	11	12
16	13	14	15	16	17	18	19
17	20	21	22	23	24	25	26
18	27	28	29	30			

May

KW	Mo	Ti	Mi	Do	Fr	Sa	So
18					1	2	3
19	4	5	6	7	8	9	10
20	11	12	13	14	15	16	17
21	18	19	20	21	22	23	24
22	25	26	27	28	29	30	31

June

KW	Mo	Ti	Mi	Do	Fr	Sa	So
23	1	2	3	4	5	6	7
24	8	9	10	11	12	13	14
25	15	16	17	18	19	20	21
26	22	23	24	25	26	27	28
27	29	30					

July

KW	Mo	Ti	Mi	Do	Fr	Sa	So
27		1	2	3	4	5	
28	6	7	8	9	10	11	12
29	13	14	15	16	17	18	19
30	20	21	22	23	24	25	26
31	27	28	29	30	31		

August

KW	Mo	Ti	Mi	Do	Fr	Sa	So
31						1	2
32	3	4	5	6	7	8	9
33	10	11	12	13	14	15	16
34	17	18	19	20	21	22	23
35	24	25	26	27	28	29	30
36	31						

September

KW	Mo	Ti	Mi	Do	Fr	Sa	So
36		1	2	3	4	5	6
37	7	8	9	10	11	12	13
38	14	15	16	17	18	19	20
39	21	22	23	24	25	26	27
40	28	29	30				

October

KW	Mo	Ti	Mi	Do	Fr	Sa	So
40				1	2	3	4
41	5	6	7	8	9	10	11
42	12	13	14	15	16	17	18
43	19	20	21	22	23	24	25
44	26	27	28	29	30	31	

November

KW	Mo	Ti	Mi	Do	Fr	Sa	So
44						1	
45	2	3	4	5	6	7	8
46	9	10	11	12	13	14	15
47	16	17	18	19	20	21	22
48	23	24	25	26	27	28	29
49	30						

December

KW	Mo	Ti	Mi	Do	Fr	Sa	So
49		1	2	3	4	5	6
50	7	8	9	10	11	12	13
51	14	15	16	17	18	19	20
52	21	22	23	24	25	26	27
53	28	29	30	31			

Impact on International Rail Freight

- Deviations: via Bressoux-Kinkempois-Leuven (TLC)
- Estimated extra running time: tbd
- Restrictions for ad-hoc requests might occur
- Restrictions in train parameters: Class 66 weight limit to 1760 ton towards Aachen
- Restrictions in container profile: yes
 - needs C60, C390, P60, P380
- In annual timetable: YES


Impact of TCR 2020 at Infrabel

Section Antwerpen - Montzen



State of play : 20.12.2019

Disclaimer see front page

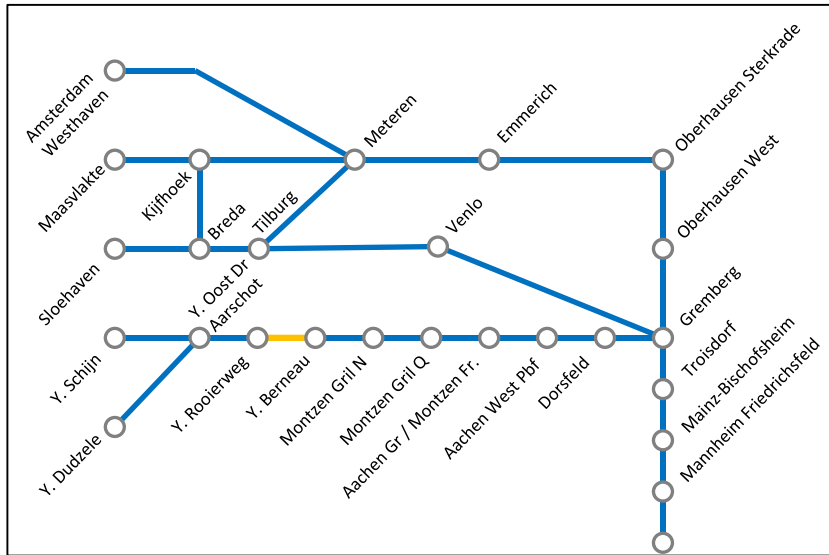

Major Capacity Restriction

- Section: Antwerpen – Montzen
- Type: Single track operation
- Duration : Continuous (see calendar)
- Type of works: Renewal of bridge and ballast

Location Bassenge - Visé

Works: renewing of bridge and ballast

Single track operation Total closure

January							February							March							April										
KW	Mo	Ti	Mi	Do	Fr	Sa	So	KW	Mo	Ti	Mi	Do	Fr	Sa	So	KW	Mo	Ti	Mi	Do	Fr	Sa	So	KW	Mo	Ti	Mi	Do	Fr	Sa	So
1			1	2	3	4	5	5						1	2	9						1	14			1	2	3	4	5	
2	6	7	8	9	10	11	12	6	3	4	5	6	7	8	9	10	2	3	4	5	6	7	8	15	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19	7	10	11	12	13	14	15	16	11	9	10	11	12	13	14	15	16	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26	8	17	18	19	20	21	22	23	12	16	17	18	19	20	21	22	17	20	21	22	23	24	25	26
5	27	28	29	30	31			9	24	25	26	27	28	29		13	23	24	25	26	27	28	29	18	27	28	29	30			
																14	30	31													

May							June							July							August										
KW	Mo	Ti	Mi	Do	Fr	Sa	So	KW	Mo	Ti	Mi	Do	Fr	Sa	So	KW	Mo	Ti	Mi	Do	Fr	Sa	So	KW	Mo	Ti	Mi	Do	Fr	Sa	So
18						1	2	3	23	1	2	3	4	5	6	27	1	2	3	4	5		31					1	2		
19	4	5	6	7	8	9	10	24	8	9	10	11	12	13	14	28	6	7	8	9	10	11	12	32	3	4	5	6	7	8	9
20	11	12	13	14	15	16	17	25	15	16	17	18	19	20	21	29	13	14	15	16	17	18	19	33	10	11	12	13	14	15	16
21	18	19	20	21	22	23	24	26	22	23	24	25	26	27	28	30	20	21	22	23	24	25	26	34	17	18	19	20	21	22	23
22	25	26	27	28	29	30	31	27	29	30						31	27	28	29	30	31			35	24	25	26	27	28	29	30
																								36	31						

September							October							November							December										
KW	Mo	Ti	Mi	Do	Fr	Sa	So	KW	Mo	Ti	Mi	Do	Fr	Sa	So	KW	Mo	Ti	Mi	Do	Fr	Sa	So	KW	Mo	Ti	Mi	Do	Fr	Sa	So
36		1	2	3	4	5	6	40						1	2	44						1	49	1	2	3	4	5	6		
37	7	8	9	10	11	12	13	41	5	6	7	8	9	10	11	45	2	3	4	5	6	7	8	50	7	8	9	10	11	12	13
38	14	15	16	17	18	19	20	42	12	13	14	15	16	17	18	46	9	10	11	12	13	14	15	51	14	15	16	17	18	19	20
39	21	22	23	24	25	26	27	43	19	20	21	22	23	24	25	47	16	17	18	19	20	21	22	52	21	22	23	24	25	26	27
40	28	29	30					44	26	27	28	29	30	31		48	23	24	25	26	27	28	29	53	28	29	30	31			
																49	30														

Impact on International Rail Freight

- Deviations: no
- Estimated extra running time: Not applicable
- Restrictions for ad-hoc requests might occur
- Restrictions in train parameters: : Class 66 weight limit to 1760 ton towards Aachen
- Restrictions in container profile: no
- In annual timetable: YES


Impact of TCR 2020 at DB Netz AG

Section Emmerich Grenze - Oberhausen Hbf



State of play : 19.12.2019

Disclaimer see front page

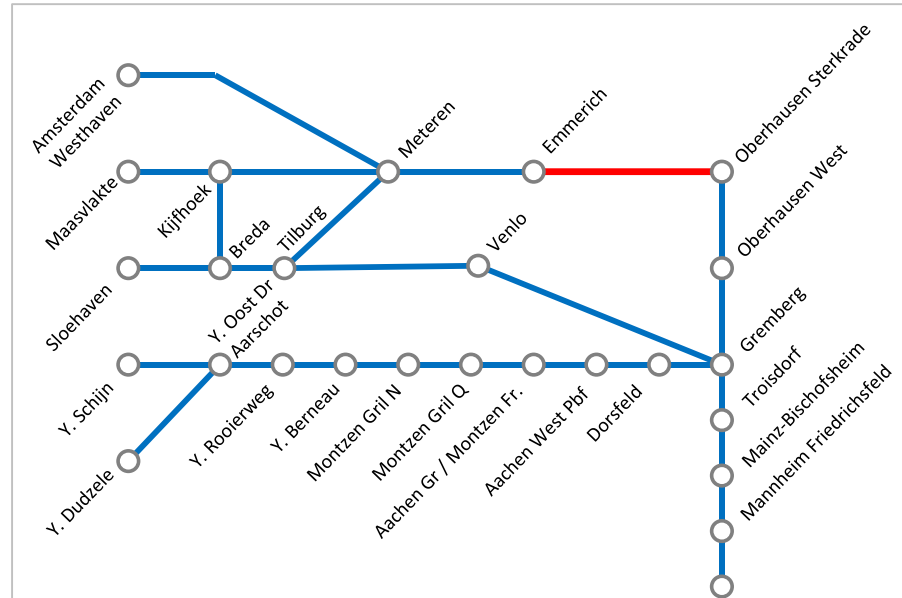

Major Capacity Restriction

- Section: Emmerich Grenze - Oberhausen Hbf
- Typ: Total Closure, Single Track Operation
- Period: Jan – Dec 2020
- Type of works: Track & Rail, Bridge, Miscellaneous

Section: Emmerich Grenze - Oberhausen Hbf

Works: Track & Rail, Bridge, Miscellaneous

Single track operation Total closure

January							February							March							April						
KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa
1			1	2	3	4	1						1	2							3						
2	6	7	8	9	10	11	3	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	
3	13	14	15	16	17	18	4	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	
4	20	21	22	23	24	25	5	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31					
5	27	28	29	30	31		6	24	25	26	27	28	29	30	31												
May							June							July							August						
KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa
18							23	1	2	3	4	5	6	27	1	2	3	4	5	6	28	1	2	3	4	5	6
19	4	5	6	7	8	9	24	8	9	10	11	12	13	28	6	7	8	9	10	11	29	3	4	5	6	7	8
20	11	12	13	14	15	16	25	15	16	17	18	19	20	29	13	14	15	16	17	18	30	10	11	12	13	14	15
21	18	19	20	21	22	23	26	22	23	24	25	26	27	30	20	21	22	23	24	25	31	17	18	19	20	21	22
22	25	26	27	28	29	30	27	29	30					31	27	28	29	30	31			24	25	26	27	28	29
September							Oktober							November							December						
KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa
36							40							44							48						
37	7	8	9	10	11	12	41	1	2	3	4	5	6	45	1	2	3	4	5	6	49	1	2	3	4	5	6
38	14	15	16	17	18	19	42	8	9	10	11	12	13	46	8	9	10	11	12	13	50	7	8	9	10	11	12
39	21	22	23	24	25	26	43	15	16	17	18	19	20	47	15	16	17	18	19	20	51	14	15	16	17	18	19
40	28	29	30				44	22	23	24	25	26	27	48	22	23	24	25	26	27	52	21	22	23	24	25	26
														49	28	29	30	31									

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB Netz individually for every customer for each affected train. Additionally DB Netz offers train path advice free of charge
- In annual timetable: No


Impact of TCR 2020 at DB Netz AG

Section Oberhausen West – Troisdorf



State of play : 19.12.2019

Disclaimer see front page

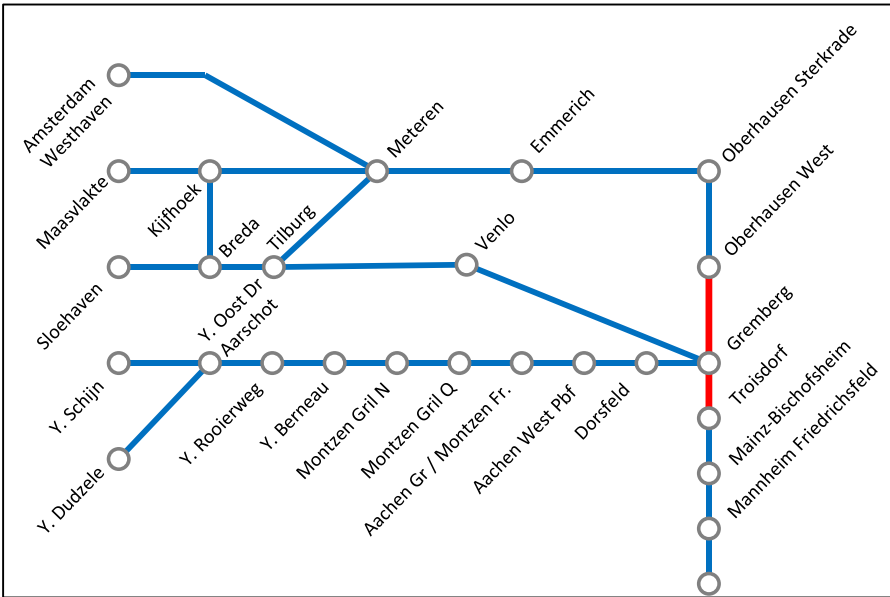

Major Capacity Restriction

- Section: Duisburg-Wedau – Troisdorf
- Typ: Total Closure, Single Track Operation
- Period: 11-05-2020 / 25-05-2020;
17-08-2020 / 27-09-2020
01-11-2020 / 23-11-2020
- Type of works: Catenary, Track & Rail, Switch, Miscellaneous

Section: Duisburg-Wedau – Troisdorf

Works: Catenary, Track & Rail, Switch, Miscellaneous

Single track operation Total closure

January							February							March							April						
KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa
1			1	2	3	4	5	1			1	2		1			1			1	1			1	2	3	4
2	6	7	8	9	10	11	12	6	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	
3	13	14	15	16	17	18	19	7	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	
4	20	21	22	23	24	25	26	8	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31				
5	27	28	29	30	31			9	24	25	26	27	28	29													
May							June							July							August						
KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa
18				1	2	3	23	1	2	3	4	5	6	7	27	1	2	3	4	5	6	31			1	2	3
19	4	5	6	7	8	9	10	24	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	
20	11	12	13	14	15	16	17	25	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31		
21	18	19	20	21	22	23	24	26	22	23	24	25	26	27	28	29	30	31									
22	25	26	27	28	29	30	31	27	29	30	31																
September							Oktober							November							December						
KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	KW	Mo	Di	Mi	Do	Fr	Sa
36			1	2	3	4	40			1	2	3	4	44			1	2	3	4	48			1	2	3	
37	7	8	9	10	11	12	41	5	6	7	8	9	10	11	45	2	3	4	5	6	7	8	9	10	11	12	
38	14	15	16	17	18	19	20	42	12	13	14	15	16	17	46	9	10	11	12	13	14	15	16	17	18	19	
39	21	22	23	24	25	26	27	43	19	20	21	22	23	24	47	16	17	18	19	20	21	22	23	24	25	26	
40	28	29	30				44	26	27	28	29	30	31	48	23	24	25	26	27	28	29	30	31				

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB Netz individually for every customer for each affected train. Additionally DB Netz offers train path advice free of charge
- In annual timetable: No


Impact of TCR 2020 at DB Netz AG

Section Cologne area



State of play : 19.12.2019

Disclaimer see front page

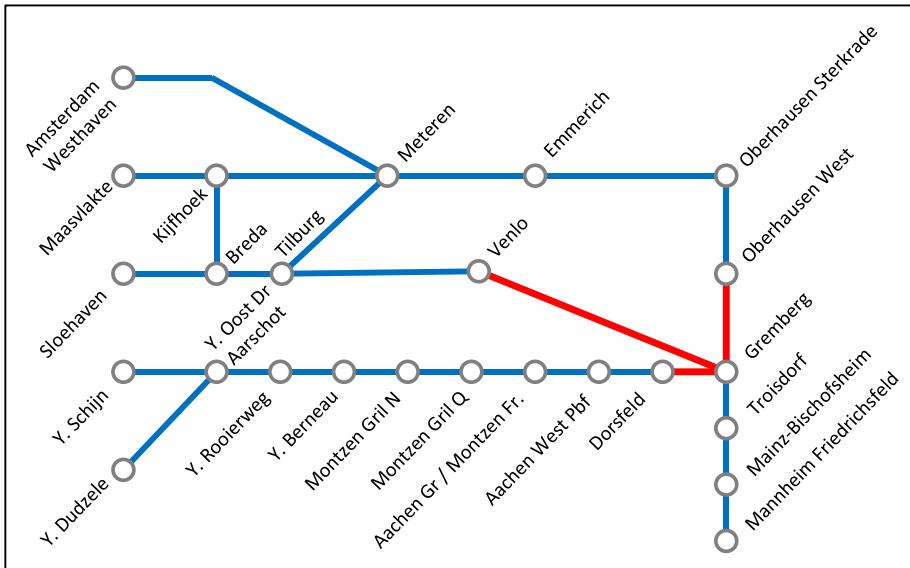

Major Capacity Restriction

- Section: Köln-Ehrenfeld Gbf – Köln Südbrücke (incl. connecting lines Köln-Longerich - Hürth-Kalscheuren and Köln-Kalk Nord Ksf)
- Typ: Total Closure, Single Track Operation
- Period: 28-02-2020 / 01-03-2020;
20-07-2010 / 27-09-2020
09-10-2020 / 26-10-2020
- Type of works: Signal, Switch, Miscellaneous

Section: Köln-Ehrenfeld Gbf – Köln Südbrücke

Works: Signal, Switch, Miscellaneous

Single track operation Total closure

January							February							March							April										
KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su
1			1	2	3	4	5	1						1	2	1							1			1	2	3	4	5	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		10	2	3	4	5	6	7	8	15	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19	4	10	11	12	13	14	15	16	11	9	10	11	12	13	14	15	16	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26	5	17	18	19	20	21	22	23	12	16	17	18	19	20	21	22	17	20	21	22	23	24	25	26
5	27	28	29	30	31			6	24	25	26	27	28	29		13	23	24	25	26	27	28	29	18	27	28	29	30			
																14	30	31													

May							June							July							August										
KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su
18						1	2	3	23	1	2	3	4	5	6	3							31								
19	4	5	6	7	8	9	10	4	8	9	10	11	12	13	14	3	6	7	8	9	10	11	4	10	11	12	13	14	15	16	
20	11	12	13	14	15	16	17	5	15	16	17	18	19	20	21	4	13	14	15	16	17	18	5	14	15	16	17	18	19	20	
21	18	19	20	21	22	23	24	6	22	23	24	25	26	27	28	5	20	21	22	23	24	25	26	6	21	22	23	24	25	26	27
22	25	26	27	28	29	30	31		29	30	31					6	27	28	29	30	31			7	24	25	26	27	28	29	30

September							Oktober							November							December										
KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su
36			1	2	3	4	5	6	4							4							4								
37	7	8	9	10	11	12	13	5	5	6	7	8	9	10	11	4	2	3	4	5	6	7	5	7	8	9	10	11	12	13	
38	14	15	16	17	18	19	20	6	12	13	14	15	16	17	18	5	9	10	11	12	13	14	6	14	15	16	17	18	19	20	
39	21	22	23	24	25	26	27	7	19	20	21	22	23	24	25	6	16	17	18	19	20	21	7	21	22	23	24	25	26	27	
40	28	29	30						26	27	28	29	30	31		7	23	24	25	26	27	28	8	28	29	30	31				

Impact on International Rail Freight

- Cancellations: No
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB Netz individually for every customer for each affected train. Additionally DB Netz offers train path advice free of charge
- In annual timetable: No

Impact of TCR 2020 at SBB Infra/BLS Netz

Section Spiez – Brig (mountain line)



State of play : 17.12.2019

Disclaimer see front page



Major Capacity Restriction

- Section: SPIEZ – BRIG (mountain line)
- Type: 1/6 tunnel closure with partially single track, from Oct – Dez 3/6 tunnel closure
- Type of Works: Tunnel renewal
- Period: From 31/07/2018 to 2022

Impact on International Rail Freight

- Reduction of available capacity; possible delays due speed reduction
- Possible rerouting rail freight via “Luino” and “Chiasso” necessary, if the requested capacity in some hours is not enough
- Marginal residual capacity during works
- in the annual TT: Yes
- Extra running time max 30 Min
- Profile restrictions No

Locations: Spiez - Brig

Works: Tunnel Renewal P/C80

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					29	30	31					29	30	31					29	30	31				

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					29	30	31					29	30	31					29	30	31				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					29	30	31					29	30	31					29	30	31				

Impact of TCR 2020 at SBB Infra/BLS Netz

Section Lugano – Mendrisio



State of play : 17.12.2019

Disclaimer see front page



Locations: Lugano - Chiasso

Works: Tunnel Renewal P/C80

Single track operation

Total closure

January

km	Mo	Tu	We	Th	Fr	Sa	Su
1			1	2	3	4	5
2	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26
5	27	28	29	30	31		

February

km	Mo	Tu	We	Th	Fr	Sa	Su
1					1	2	
2	3	4	5	6	7	8	
3	9	10	11	12	13	14	15
4	16	17	18	19	20	21	22
5	23	24	25	26	27	28	29

March

km	Mo	Tu	We	Th	Fr	Sa	Su
1							1
2	2	3	4	5	6	7	8
3	9	10	11	12	13	14	15
4	16	17	18	19	20	21	22
5	23	24	25	26	27	28	29
6	30	31					

April

km	Mo	Tu	We	Th	Fr	Sa	Su
1			1	2	3	4	
2	5	6	7	8	9	10	11
3	12	13	14	15	16	17	18
4	19	20	21	22	23	24	25
5	26	27	28	29	30		

May

km	Mo	Tu	We	Th	Fr	Sa	Su
1			1	2	3		
2	4	5	6	7	8	9	10
3	11	12	13	14	15	16	17
4	18	19	20	21	22	23	24
5	25	26	27	28	29	30	31

June

km	Mo	Tu	We	Th	Fr	Sa	Su
1	1	2	3	4	5	6	7
2	8	9	10	11	12	13	14
3	15	16	17	18	19	20	21
4	22	23	24	25	26	27	28
5	29	30					

July

km	Mo	Tu	We	Th	Fr	Sa	Su
1			1	2	3	4	5
2	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26
5	27	28	29	30			

August

km	Mo	Tu	We	Th	Fr	Sa	Su
1							1
2	2	3	4	5	6	7	8
3	9	10	11	12	13	14	15
4	16	17	18	19	20	21	22
5	23	24	25	26	27	28	29
6	30	31					

September

km	Mo	Tu	We	Th	Fr	Sa	Su
1			1	2	3	4	5
2	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26
5	27	28	29	30			

October

km	Mo	Tu	We	Th	Fr	Sa	Su
1					1	2	3
2	4	5	6	7	8	9	10
3	11	12	13	14	15	16	17
4	18	19	20	21	22	23	24
5	25	26	27	28	29	30	31

November

km	Mo	Tu	We	Th	Fr	Sa	Su
1							1
2	2	3	4	5	6	7	8
3	9	10	11	12	13	14	15
4	16	17	18	19	20	21	22
5	23	24	25	26	27	28	29

December

km	Mo	Tu	We	Th	Fr	Sa	Su
1			1	2	3	4	5
2	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26
5	27	28	29	30	31		

Major Capacity Restriction

- Section: LUGANO - MENDRISIO
- Type: Single track night and day
- Works: finalization P/C80 Paradiso/S. Martino tunnel
- Period: 05.01.2019 – 12.12.2020

Impact on International Rail Freight

- Reduction of available capacity
- Rerouting rail freight via “Luino and Domodossola” will be possible
- In the annual TT: Yes
- Extra running time depending of capacity via Luino and Domodossola
- Profile restrictions No


Impact of TCR 2020 at SBB Infra/BLS Netz

Section Brig – Iselle



State of play : 17.12.2019

Disclaimer see front page

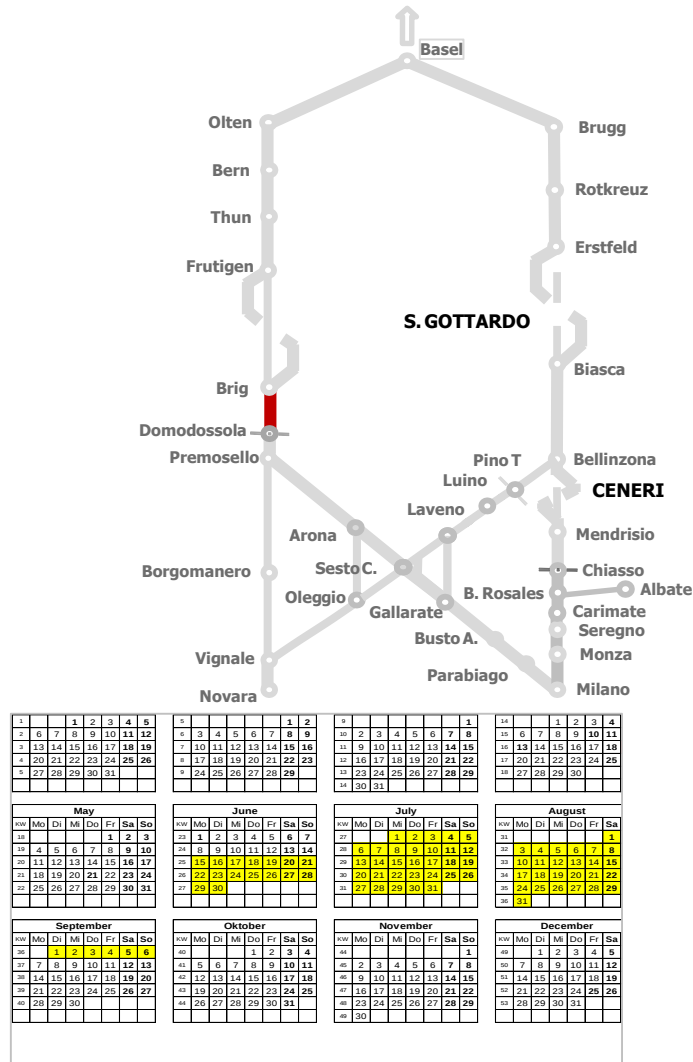

Major Capacity Restriction

- Section: BRIG - ISELLE
- Type: Single track night and day
- Works: Simplon tunnel renewal
- Period: 14.06.2020 – 06.09.2020

Impact on International Rail Freight

- Reduction of available capacity
- Rerouting rail freight mostly via “Chiasso and a small part via Luino” will be possible
- In the annual TT: Yes
- Extra running time depending of capacity via Chiasso and Luino
- Profile restrictions: No, but rerouting of trains with P/C80 is not possible via Gotthard

Impact of TCR 2020 RFI

Section Iselle – Varzo (Elicoidale Tunnel)



State of play : 12.2019

Disclaimer see front page



Locations: Iselle - Varzo (Elicoidale Tunnel)

Works: Tunnel securing

Single track operation Total closure

January							February							March							April										
km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So
1			1	2	3	4	5	6						1	2	7							1			1	2	3	4	5	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		2	3	4	5	6	7	8	1	6	7	8	9	10	11	12	
3	13	14	15	16	17	18	19	10	11	12	13	14	15	16	17	11	10	11	12	13	14	15	12	13	14	15	16	17	18	19	
4	20	21	22	23	24	25	26	17	18	19	20	21	22	23	24	12	13	14	15	16	17	18	13	20	21	22	23	24	25	26	
5	27	28	29	30	31			24	25	26	27	28	29			14	23	24	25	26	27	28	29	14	27	28	29	30			

May							June							July							August										
km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So
1						1	2	3	1	2	3	4	5	6	7	1							1								
2	4	5	6	7	8	9	10	8	9	10	11	12	13	14		2	3	4	5	6	7	8	2	3	4	5	6	7	8	9	
3	11	12	13	14	15	16	17	15	16	17	18	19	20	21	22	3	4	5	6	7	8	9	4	5	6	7	8	9	10	11	
4	18	19	20	21	22	23	24	22	23	24	25	26	27	28	29	10	11	12	13	14	15	16	12	13	14	15	16	17	18	19	
5	25	26	27	28	29	30	31	27	28	29	30	31				16	17	18	19	20	21	22	13	14	15	16	17	18	19	20	

September							October							November							December										
km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So
1								1								1							1								
2	7	8	9	10	11	12	13	2	3	4	5	6	7	8	9	2	3	4	5	6	7	8	2	3	4	5	6	7	8	9	
3	14	15	16	17	18	19	20	9	10	11	12	13	14	15	16	3	4	5	6	7	8	9	3	4	5	6	7	8	9	10	
4	21	22	23	24	25	26	27	16	17	18	19	20	21	22	23	10	11	12	13	14	15	16	4	5	6	7	8	9	10	11	
5	28	29	30					23	24	25	26	27	28	29	30	17	18	19	20	21	22	23	5	6	7	8	9	10	11	12	

November							December								
km	Mo	Di	Mi	Do	Fr	Sa	So	km	Mo	Di	Mi	Do	Fr	Sa	So
1								1							
2	2	3	4	5	6	7	8	2	3	4	5	6	7	8	9
3	9	10	11	12	13	14	15	3	4	5	6	7	8	9	10
4	16	17	18	19	20	21	22	11	12	13	14	15	16	17	18
5	23	24	25	26	27	28	29	18	19	20	21	22	23	24	25

Major Capacity Restriction

- Section: Iselle– Varzo (Elicoidale Tunnel)
- Type: 21d total tunnel closure, from Aug – Sept
- Type of Works: Tunnel securing
- Period: From 16.08.2020 to 06.09.2020

Impact on International Rail Freight

- Cancellation of trains with profile P/C80 via Domodossola
- Necessary rerouting rail freight via “Luino” and “Chiasso”
- In the annual TT: YES
- Profile restrictions: Yes

Impact of TCR 2020 RFI

Section Iselle – Varzo (2)



State of play : 12.2019
Disclaimer see front page



Locations: Iselle - Varzo
Works: Track renewal

Legend: ■ Single track operation ■ Total closure ■ Line interruption + single track circulation (in a few hours)

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					29	30	31					29	30	31					29	30	31				

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					29	30	31					29	30	31					29	30	31				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					29	30	31					29	30	31					29	30	31				

Major Capacity Restriction

- Section: Iselle – Varzo
- Type: n°60 line interruptions of 240' in daytime period + 1h of single track circulation) + 7 barrages / month of 300'
- Type of Works: track renewal
- Period: 7 January - 27 March 2020

Impact on International Rail Freight

- Cancellation of trains with profile P/C80 via Domodossola in daytime operations
- Necessary rerouting rail freight in daytime via "Luino" and "Chiasso"
- In the annual TT: YES
- Profile restrictions: NO


Impact of TCR 2020 RFI

Section Sesto C. – Gallarate (Vergiate Tunnel)



State of play : 12.2019

Disclaimer see front page

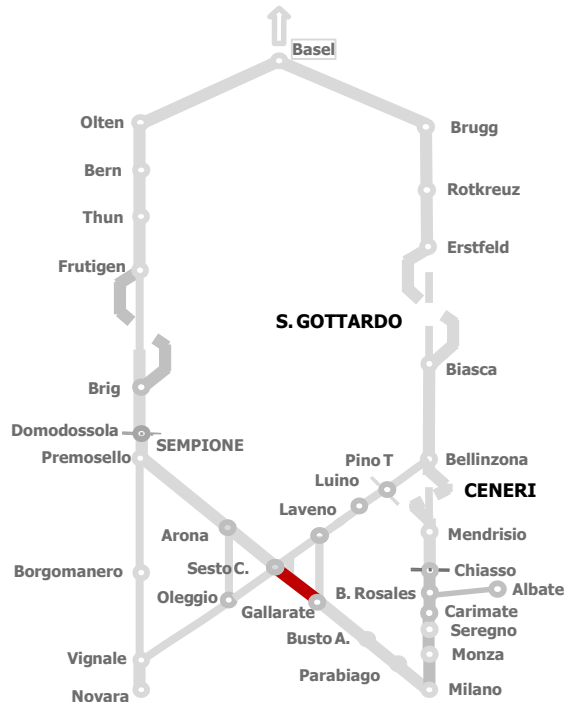

Locations: Sesto C. - Gallarate (Galleria di Vergiate)

Works: Tunnel Renewal P/C80

Yellow box: Single track operation Red box: Total closure

January							February							March							April										
km	Mo	Tu	We	Th	Fr	Sa	So	km	Mo	Tu	We	Th	Fr	Sa	So	km	Mo	Tu	We	Th	Fr	Sa	So	km	Mo	Tu	We	Th	Fr	Sa	So
1			1	2	3	4	5	6						1	2	7							1	2	3	4	5				
6	7	8	9	10	11	12		3	4	5	6	7	8	9		2	3	4	5	6	7	8	9	10	11	12					
13	14	15	16	17	18	19		10	11	12	13	14	15	16		9	10	11	12	13	14	15	16	17	18	19					
20	21	22	23	24	25	26		17	18	19	20	21	22	23		16	17	18	19	20	21	22	23	24	25	26					
27	28	29	30	31				24	25	26	27	28	29		23	24	25	26	27	28	29		27	28	29	30					

May							June							July							August										
km	Mo	Tu	We	Th	Fr	Sa	So	km	Mo	Tu	We	Th	Fr	Sa	So	km	Mo	Tu	We	Th	Fr	Sa	So	km	Mo	Tu	We	Th	Fr	Sa	So
1						1	2	3	1	2	3	4	5	6	7	21	1	2	3	4	5		21								
4	5	6	7	8	9	10		8	9	10	11	12	13	14		18	19	20	21	22	23	24	25	26	27	28	29	30			
11	12	13	14	15	16	17		15	16	17	18	19	20	21		15	16	17	18	19	20	21	22	23	24	25	26	27			
18	19	20	21	22	23	24		22	23	24	25	26	27	28		22	23	24	25	26	27	28	29	30	31						
25	26	27	28	29	30	31		29	30							29	30														

September							October							November							December										
km	Mo	Tu	We	Th	Fr	Sa	So	km	Mo	Tu	We	Th	Fr	Sa	So	km	Mo	Tu	We	Th	Fr	Sa	So	km	Mo	Tu	We	Th	Fr	Sa	So
1			1	2	3	4	5	4						1	2	1							1	2	3	4	5	6			
7	8	9	10	11	12	13		5	6	7	8	9	10	11		2	3	4	5	6	7	8	7	8	9	10	11	12	13		
14	15	16	17	18	19	20		12	13	14	15	16	17	18		9	10	11	12	13	14	15	14	15	16	17	18	19	20		
21	22	23	24	25	26	27		19	20	21	22	23	24	25		16	17	18	19	20	21	22	21	22	23	24	25	26	27		
28	29	30						26	27	28	29	30	31		23	24	25	26	27	28	29		28	29	30	31					

Major Capacity Restriction

- Section: Sesto C. - Gallarate (Vergiate Tunnel)
- Type: 70 days int. even track and 30 days int. odd track (Jun. 2020 – Sept. 2020) with preparatory and completion works in 4h night interruptions (Dec.2020)
- Type of Works: Adjustment to P/C 80 Vergiate tunnel
- Period: From 14/06/2020 to 20/09/2020

Impact on International Rail Freight


- Reduction of available capacity
- Marginal residual capacity during works
- in the annual TT: NO
- Extra running time max 30 Min

Impact of TCR 2020 RFI

Section Pino Tronzano - Oleggio



State of play : 12.2019
Disclaimer see front page

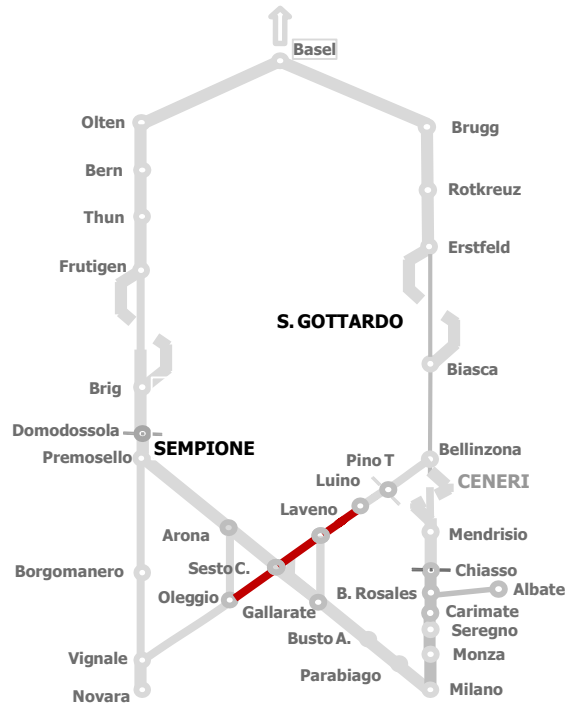

Major Capacity Restriction

- Section: Pino Tronzano - Oleggio
- Type: daytime interruptions of 240' / 300'
- (Range 08.40 - 13.00 approx.) (From Mon - Fri, including Wednesday) with the except for period 16 August - 6 September.
- Works: ACC & mod.750 + station Maccagno renew
- Period: 14.06.2020 – 31.12.2020

Impact on International Rail Freight

- Reduction of available capacity
- Rerouting rail freight will be possibile
- In the annual TT: Yes
- Extra running time max 30'
- Profile restrictions No

Locations: Pino Tronzano - Oleggio

Works: ACC & mod.750

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1		2	3	4	5		6					1	2	3						1	2	3	4	5	6	7	8
9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4	5	6
7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4
13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31									
20	21	22	23	24	25	26	27	28	29	30	31																
27	28	29	30	31																							

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28
18	19	20	21	22	23	24	25	26	27	28	29	30	31														
25	26	27	28	29	30	31																					


September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28
24	25	26	27	28	29	30	31																				
31																											

Section Bivio Fegino-S.Quirico (TerzoValico dei Giovi)



State of play : 12.2019

Disclaimer see front page

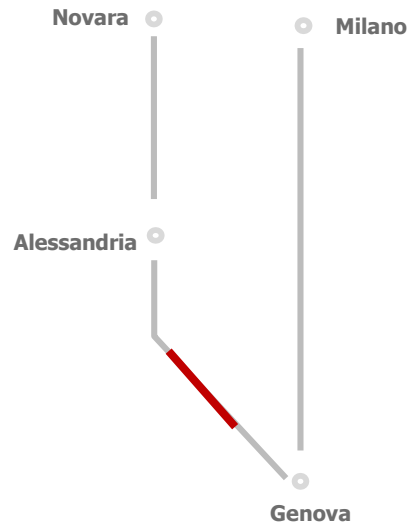

Major Capacity Restriction

- Section: Bivio Fegino-S.Quirico
- Type: Line interruption of 45 days
- Works: Terzo Valico dei Giovi
- Period: 24 Jul. 2020 – 06 Sep. 2020

Impact on International Rail Freight

- Total closure
- In the annual TT: NO
- Profile restrictions: No, but rerouting is possible

Locations: Bivio Fegino-S.Quirico

Works: Terzo-Valico dei Giovi

 Single track operation  Total closure

January							February							March							April										
KW	Mo	Di	Mi	Do	Fr	Sa	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	Sa
1			1	2	3	4	5	6						1	2	9						1	14			1	2	3	4	5	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9	10	10	2	3	4	5	6	7	8	15	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19	10	11	12	13	14	15	16	17	11	9	10	11	12	13	14	15	16	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26	17	18	19	20	21	22	23	24	12	10	17	18	19	20	21	22	17	18	19	20	21	22	23	24
5	27	28	29	30	31			24	25	26	27	28	29			13	23	24	25	26	27	28	29	18	27	28	29	30			
																14	30	31													

May							June							July							August										
KW	Mo	Di	Mi	Do	Fr	Sa	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	Sa
18						1	2	19	1	2	3	4	5	6	7	27	27					1	2	3	31						
19	4	5	6	7	8	9	10	20	8	9	10	11	12	13	14	28	6	7	8	9	10	11	12	32	1	2	3	4	5	6	
20	11	12	13	14	15	16	17	21	15	16	17	18	19	20	21	29	13	14	15	16	17	18	19	33	8	9	10	11	12	13	
21	18	19	20	21	22	23	24	22	22	23	24	25	26	27	28	30	20	21	22	23	24	25	26	34	17	18	19	20	21	22	23
22	25	26	27	28	29	30	31	23	29	30						31	27	28	29	30	31			35	24	25	26	27	28	29	30
																								36	1	2	3	4	5	6	7

September							October							November							December										
KW	Mo	Di	Mi	Do	Fr	Sa	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	Sa	KW	Mo	Di	Mi	Do	Fr	Sa	Sa
23	1	2	3	4	5	6	7	40				1	2	3	4	44						1	49			1	2	3	4	5	6
24	7	8	9	10	11	12	13	41	5	6	7	8	9	10	11	45	2	3	4	5	6	7	8	50	7	8	9	10	11	12	13
25	14	15	16	17	18	19	20	42	12	13	14	15	16	17	18	46	9	10	11	12	13	14	15	51	14	15	16	17	18	19	20
26	21	22	23	24	25	26	27	43	19	20	21	22	23	24	25	47	16	17	18	19	20	21	22	52	21	22	23	24	25	26	27
27	28	29	30					44	26	27	28	29	30	31		48	23	24	25	26	27	28	29	53	28	29	30	31			

Links to national TCR information

NL: www.prorail.nl/projecten

BE: to log in an account is needed

www.infrabel.be/en/professionals/rail-operators/business-corner

DE: [http://fahrweg.dbnetze.com/fahrweg-en/customers/construction site information/](http://fahrweg.dbnetze.com/fahrweg-en/customers/construction_site_information/)

CH: www.trasse.ch/dienstleistungen/zuteilung

IT: to log in an account is needed: <https://pir.rfi.it/pir>
